Hare Krishna

Prasadam, Sweets & Savories Vertical

Project Management Plan

Hare Krishna Golden Temple (ISKCON), Banjara Hills, Hyderabad

Prepared for: Temple management, Production (Prabhu) and DMTT

Source: Prasadam Revenue Generation Plan meeting, 26 September 2026

v1.2, 21 October 2026

Figures marked [ESTIMATE] are planning assumptions. Replace them with the 6–12 month order data before committing budget.

Contents

1. Project charter

2. Objectives and success criteria

3. Scope

4. Stakeholders

5. Organisation and RACI

6. Work breakdown structure and schedule

7. Milestones

8. Budget

9. Risk register

10. Quality management

11. Communication plan

12. Governance and reporting

13. Change control

14. Issue and decision log

15. Action items

1. Project charter

Field	Detail
Project name	Prasadam, Sweets & Savories Vertical launch
Organisation	Hare Krishna Golden Temple (ISKCON), Banjara Hills, Hyderabad
Sponsor	Temple leadership
Project lead	Mukunda Dasa (marketing, sales, technology)
Production lead	Prabhu (temple production)
Start / pilot end / Year-1 end	26 Sep 2026 / 30 Nov 2026 / 30 Sep 2027
Purpose	Offer pure, satvik, preservative-free prasadam, prepared with devotion and offered to Sri Sri Radha Krishna, to every audience we already touch: visitors, donors, devotees, companies, institutions, communities and online buyers. Production is done by the temple kitchen; marketing, technology and sales are done by the DMTT; every rupee and hour is tracked for ROI.
Business case	Proven festival demand, strong brand, warm B2B network and existing systems; two-tier pricing makes the kitchen viable; Year-1 revenue about ₹2.2 crore [ESTIMATE].
Key constraints	Kitchen capacity (4 staff), no historic cost data compiled, festival deadlines fixed, brand-use approval needed.
Assumptions	Departments move all prasadam orders in-house; B2B orders take 50% advance; seasonal staff available at short notice.

2. Objectives and success criteria

#	Objective	Success criterion
O1	Launch the vertical with a ready sales kit	Catalogue, prices, samples and packaging ready by 10 Oct 2026
O2	Win Dasara/Diwali corporate orders	≥ 5,000 gift boxes and ≥ 10 corporate/institution clients by 8 Nov 2026 [ESTIMATE]
O3	Stabilise internal supply	100% of internal prasadam orders placed with in-house production by Nov 2026
O4	Go online	Shopify + Amazon live with ≥ 12 SKUs by 31 Jan 2027
O5	10× festival counters	Janmashtami 2027 counter sales ≥ ₹60 lakh (10× 2026) as stretch; ₹30 lakh base
O6	Prove ROI	Monthly DMTT ROI report from Nov 2026; vertical cash-positive by month 6
O7	Year-1 revenue	₹2.2 crore gross revenue Oct 2026–Sep 2027 [ESTIMATE]

3. Scope

In scope

- Sweets, savories, gift boxes, pickles/papads/powders
- Internal supply, festival stalls, restaurant/lawn, corporate & white-label gifting
- E-commerce, gated communities, outbound B2B, catering (pilot scale), donor packs
- Packaging, pricing, marketing, technology, ROI tracking
- Planning for QSR partnership and exports (execution later phases)

Out of scope (Year 1)

- Building a new dedicated production facility in Year 1

- Opening QSR outlets in Year 1
- Education company, games, audio/video, advertising projects (separate initiatives)
- Dairy/ghee production (evaluate separately)

Deliverables

- Approved business plan and charter
- Demand forecast from 6–12 months of order data
- Product list, recipes, costing, price list
- Sales kit: catalogue, menu, sample boxes, white-label templates
- Festival stall SOP and layout
- Internal weekly order system
- Shopify store and Amazon listing
- ROI dashboard (monthly)
- Pilot review report
- Year-1 review and Year-2 budget

4. Stakeholders

Stakeholder	Interest	Influence	Engagement
Temple leadership	Revenue, reputation, sanctity of prasadam	High	Quarterly steering, monthly ROI
Production lead & kitchen team	Workable volumes, fair staffing	High	Weekly plan, daily in festival weeks
Production manager	Resource commitments	High	Decision meeting, monthly review
DMTT	Marketing, tech, data, ROI	High	Weekly
Internal departments	Reliable supply, price	Medium	Order cut-offs, monthly budget
Corporate clients & institutions	Quality, on-time, branding	Medium	Account management
Donors & devotees	Purity, devotion, value	Medium	Campaigns
QSR partner	Brand licence, scale	Medium	Year-2 negotiations
Regulators (FSSAI, GST)	Compliance	High	Licences, audits

5. Organisation and RACI

Role	Person	Responsibility
Executive sponsor	Temple leadership	Approves budget, brand use and major decisions
Vertical lead – marketing, sales & technology	Mukunda Dasa	Vision, network, marketing, e-commerce, DMTT reporting
Production lead	Prabhu (production)	Recipes, costing, samples, capacity, kitchen team
Production manager (reporting line)	Production lead's manager	Approves production commitments and resources
E-commerce & logistics advisor	Subhadra Radha Devi Mataji	Shopify/Amazon, fastest shipping
Corporate sales representative	To be assigned by Mukunda Dasa	Joins owner meetings; manages B2B pipeline
Order coordinator (new hire)	To hire now	Order confirmations, internal orders, production calendar
Design & packaging	DMTT designer	Catalogue, boxes, stickers, white-label mock-

		ups
Data & AI	DMTT data scientists	Demand analysis, targeting, ROI dashboard
Finance	Accounts team	Cost centre, GST, P&L, ROI
Quality & compliance	To assign	FSSAI, labelling, hygiene audits

RACI matrix

R = Responsible, A = Accountable, C = Consulted, I = Informed.

Activity	Sponsor	Mukunda Dasa	Production lead	Prod. manager	DMTT	Sales rep	Finance	Quality
Vertical strategy & budget	A	R	C	C	C	I	C	I
Product list, recipes, samples	I	C	R/A	C	I	I	I	C
Costing & pricing	I	A	R	C	C	C	C	I
Packaging & catalogue design	I	A	C	I	R	C	I	C
Corporate & white-label sales	I	A	C	I	C	R	I	I
Festival stalls	I	A	R	C	C	C	C	C
Internal weekly orders	I	A	R	I	C	I	C	I
E-commerce & logistics	I	A	C	I	R	I	C	I
Compliance (FSSAI, labels, hygiene)	I	C	R	C	I	I	I	A
ROI tracking & reporting	I	A	C	I	R	I	R	I
Hiring & staffing	I	C	R	A	I	I	C	I
Capex (pagodas, machines, unit)	A	R	C	C	I	I	C	C

6. Work breakdown structure and schedule

The same WBS, with a Gantt view, is in 05_Project_Tracker.xlsx for day-to-day updates.

ID	Task	Owner	Start	End	Depends
1	Initiation & governance		26 Sep 26	10 Oct 26	
1.1	Send detailed vertical plan to stakeholders	Mukunda Dasa	26 Sep 26	30 Sep 26	
1.2	Production lead reviews plan with his manager	Production lead	30 Sep 26	03 Oct 26	1.1
1.3	Decision meeting (Mukunda Dasa, production lead, manager)	Mukunda Dasa	05 Oct 26	05 Oct 26	1.2
1.4	Set up DMTT cost centre and ROI tracker	DMTT / Finance	29 Sep 26	06 Oct 26	
1.5	Confirm brand-use approval and FSSAI scope	Quality & compliance	29 Sep 26	09 Oct 26	
2	Demand & data		26 Sep 26	06 Oct 26	
2.1	Provide order confirmation info to production	Order coordinator	26 Sep 26	29 Sep 26	
2.2	Analyse 6–12 months prasadam purchases & volumes	DMTT data	27 Sep 26	03 Oct 26	
2.3	Estimate weekly minimum & festival peaks	DMTT data	02 Oct 26	06 Oct 26	2.2
2.4	Department budgets (LLP, Culture Connect, online donors)	Mukunda Dasa	29 Sep 26	04 Oct 26	
3	Product, costing & packaging		28 Sep 26	12 Oct 26	
3.1	Propose budget & item list to production for samples	Mukunda Dasa	28 Sep 26	30 Sep 26	
3.2	Identify more long-shelf-life products	Production lead	28 Sep 26	04 Oct 26	
3.3	Samples & costing sheets (mass & premium)	Production lead	01 Oct 26	08 Oct 26	3.1
3.4	Pricing & gift tiers finalised	Mukunda Dasa	06 Oct 26	09 Oct 26	3.3
3.5	Packaging, stickers, catalogue, menu design	DMTT designer	30 Sep 26	10 Oct 26	
3.6	Sample gift boxes assembled for pitching	Production lead	08 Oct 26	12 Oct 26	3.3,3.5

4	Resources		26 Sep 26	15 Oct 26	
4.1	Hire additional production/order person	Production lead	26 Sep 26	10 Oct 26	
4.2	Assign corporate sales representative	Mukunda Dasa	29 Sep 26	03 Oct 26	
4.3	Seasonal staff plan for Dasara/Diwali	Production lead	05 Oct 26	15 Oct 26	2.3
5	Pilot: Dasara & Diwali		10 Oct 26	30 Nov 26	
5.1	Owner meetings (companies, MNR, chambers, BNI)	Mukunda Dasa + sales rep	10 Oct 26	31 Oct 26	3.6
5.2	Serve the three companies that already asked	Sales rep	10 Oct 26	18 Oct 26	3.6
5.3	Mahalaya & Dasara stall roll-out	Production lead	08 Oct 26	20 Oct 26	4.3
5.4	Weekly internal standing orders live	Order coordinator	12 Oct 26	19 Oct 26	2.3
5.5	Diwali gift production & dispatch	Production lead	20 Oct 26	06 Nov 26	5.1
5.6	Sell leftovers online / Instagram	DMTT	09 Nov 26	20 Nov 26	5.5
5.7	Pilot review & lessons learned	Mukunda Dasa	23 Nov 26	30 Nov 26	5.6
6	Channel launch		01 Dec 26	31 Mar 27	
6.1	Shelf-life lab tests & labels	Quality & compliance	01 Dec 26	31 Dec 26	
6.2	Shopify store live	DMTT e-commerce	01 Dec 26	15 Jan 27	6.1
6.3	Amazon listing	E-commerce advisor	05 Jan 27	31 Jan 27	6.2
6.4	New Year, Vaikuntha Ekadashi & Sankranti campaigns	DMTT	10 Dec 26	15 Jan 27	
6.5	Gated community stalls (10 → 30)	Sales rep	10 Jan 27	31 Mar 27	
6.6	Catering pilot	Production lead	15 Jan 27	31 Mar 27	
6.7	CRM + B2B sales executive	Mukunda Dasa	01 Jan 27	15 Feb 27	
6.8	Subscription box beta	DMTT	01 Feb 27	31 Mar 27	6.2
7	Scale in Hyderabad		01 Apr 27	30 Sep 27	
7.1	Pagoda costing, procurement & installation	Facilities	01 Apr 27	30 Jun 27	
7.2	Pickles, papads, powders launch	Production lead	15 Apr 27	30 Jun 27	6.1
7.3	Learning visits: Mysore & Ahmedabad	Production lead	15 Apr 27	15 May 27	
7.4	Janmashtami 2027 10× plan & execution	Mukunda Dasa + Production lead	01 Jun 27	05 Sep 27	7.1
7.5	Year-1 review & Year-2 budget	Mukunda Dasa	10 Sep 27	30 Sep 27	7.4
8	Year 2+: unit, QSR, exports		01 Oct 27	30 Sep 28	
8.1	Dedicated production unit business case & build	Temple leadership	01 Oct 27	31 Mar 28	7.5
8.2	QSR brand licence & 1–3 pilots	Mukunda Dasa	01 Oct 27	30 Jun 28	7.5
8.3	Export readiness (IEC, APEDA, partners)	Mukunda Dasa	01 Jan 28	30 Sep 28	8.1

7. Milestones

Milestone	Target date	Gate criteria
M1 Plan circulated	30 Sep 2026	Plan shared with production lead and manager
M2 Decision meeting / charter signed	5 Oct 2026	Products, quantities, budget, pricing agreed
M3 Sales kit ready	12 Oct 2026	Catalogue, prices, 10 sample boxes
M4 Dasara delivered	20 Oct 2026	Stalls live, first corporate orders delivered
M5 Diwali delivered	6 Nov 2026	All Diwali orders dispatched on time
M6 Pilot review	30 Nov 2026	P&L, ROI, lessons; go/no-go for Phase 2
M7 Online store live	15 Jan 2027	Shopify live with ≥12 SKUs
M8 Pagodas installed	30 Jun 2027	Permanent stalls in place
M9 Janmashtami 2027	Sep 2027	Counter sales ≥ ₹30 L (base) / ₹60 L (stretch)
M10 Year-1 review	30 Sep 2027	Annual report and Year-2 budget approved

8. Budget [ESTIMATE]

Item	₹ lakh (Y1)	Note

Additional staff salaries	24	1 order coordinator now + seasonal cooks + sales exec (Phase 2)
Marketing (ads, content, samples)	12	≈5% of revenue
Packaging design & moulds	3	One-time catalogue, dies, stickers
Pagodas & stall kits	6	Rain-proof pagodas, tables, signage, POS
Technology (Shopify, apps, POS, CRM)	3	Subscriptions and integrations
Utilities & kitchen overheads (allocated)	8	Power, gas, water, maintenance
Compliance, testing, licences	2	Shelf-life tests, FSSAI, audits
Logistics not charged to customers	5	Free-shipping offers, B2B deliveries
Contingency	4	≈5%
Total opex	67	

Capex item	Estimate	When
Small machines (chikki cutter, laddu maker, sealing, packing)	₹8–15 L	Phase 2–3
Permanent pagodas (8–12 units)	₹6–12 L	Phase 3
Storage racks, dehumidifier, weighing & labelling	₹3–5 L	Phase 2
Dedicated production unit fit-out	₹50 L–1.5 Cr	Phase 4 (only after demand is proven)
Delivery vehicle	₹8–12 L	Phase 3–4

9. Risk register

Likelihood (L) and impact (I) on a 1–5 scale; score = L × I. Scores of 15+ are reviewed weekly.

ID	Risk	L	I	Score	Mitigation	Owner
R-01	Kitchen cannot meet Diwali peak volume	4	5	20	Forecast from order data; seasonal staff; cap orders by capacity; 50% advance; partner kitchens on standby	Production lead
R-02	Premium-only pricing fails to cover fixed costs	3	4	12	Two-tier model; mass tier for volume; monthly margin review	Mukunda Dasa
R-03	Food-safety incident harms temple reputation	2	5	10	FSSAI compliance, hygiene SOPs, batch codes, shelf-life tests, staff medical checks, recall plan	Quality
R-04	Use of the ISKCON name on commercial packaging questioned	3	4	12	Written approval from temple leadership / group legal; consistent brand guidelines; consider a sub-brand	Sponsor
R-05	Perception that prasadam is being commercialised	3	3	9	Passive selling, devotional messaging, transparent use of proceeds, prasadam offered first	Mukunda Dasa
R-06	Ingredient price spikes (ghee, jaggery, nuts)	4	3	12	Forward-buy before season, two suppliers, sugar/jaggery flexibility, price validity clauses	Production lead
R-07	Festival sales below plan; leftover stock	3	3	9	Shelf-stable SKUs, pre-orders, online/Instagram clearance	DMTT
R-08	Late B2B deliveries during peak	3	4	12	Production calendar, cut-off dates, dispatch buffer, own vehicle	Order coordinator
R-09	Staff overload across departments	4	3	12	Dedicated hires; clear RACI; hours tracked in DMTT	Prod. manager
R-10	Online shipping damage/spoilage	3	3	9	Moisture-proof packs, tested courier partners, only shelf-stable items online	E-commerce advisor
R-11	Rain disrupts festival stalls	3	3	9	Rain-proof pagodas; indoor fallback locations	Facilities
R-12	Cash/stock leakage at stalls	2	3	6	UPI-first, POS, stock reconciliation per shift	Finance
R-13	QSR partner quality not aligned with temple standards	3	5	15	Strict brand licence, audits, satvik SOPs, exit clauses	Sponsor

R-14	Regulatory changes (FSSAI, GST)	2	2	4	Quarterly compliance review	Finance

10. Quality management

- Standard recipes and yield sheets for every SKU; taste panel sign-off before launch.
- Shelf-life lab test per SKU and pack type before selling online.
- Batch codes, MFD and best-before on every pack; FIFO in stores.
- Hygiene SOP: head covers, gloves, hand-wash, pest control, cleaning log; staff medical checks.
- Supplier checks for ghee, oil, jaggery, nuts; retain samples of each batch for 30 days.
- Customer complaint log with 48-hour response and root-cause review.
- Monthly internal audit; external FSSAI audit readiness.

11. Communication plan

Audience	What	How
Temple leadership	Monthly ROI report, quarterly steering deck	Email + meeting
Production team	Weekly production plan, festival forecasts	System + WhatsApp group
Internal departments	Order cut-offs, price list, delivery day	System notice
Corporate clients	Catalogue, quotes, order status	Email, WhatsApp
Donors & public	Festival campaigns, launches	WhatsApp, SMS, social, website

12. Governance and reporting

Cadence	Forum	Chair
Daily (festival weeks)	Stand-up: production + stalls + dispatch	Production lead
Weekly	Order & pipeline review (orders, production plan, sales pipeline, issues)	Mukunda Dasa
Monthly	P&L and ROI review with DMTT & finance; KPI dashboard	Mukunda Dasa + Finance
After each hero campaign	Post-campaign review and lessons learned	Vertical lead
Quarterly	Steering review with temple leadership; budget and capex decisions	Sponsor

KPI dashboard


KPI	Definition	Unit	Frequency
Revenue	Monthly gross revenue by stream	₹ lakh	Monthly
Gross margin	Revenue minus ingredients, packaging, direct labour	%	Monthly
ROI	(Contribution − DMTT & marketing cost) ÷ total invested cost	%	Monthly
Hours invested	Hours spent by DMTT, production, sales on the vertical	hours	Weekly
Festival sales	Sales per festival and per stall-hour	₹	Per event
Corporate pipeline	Leads, meetings, proposals, POs, boxes	count	Weekly
Online	Orders, conversion rate, CAC, ROAS, repeat rate	various	Weekly
Operations	On-time delivery %, order fill rate, spoilage %	%	Weekly

Quality	Complaints per 1,000 orders; audit score	count / score	Monthly
Customer	Rating, NPS, repeat B2B clients	score	Quarterly


DMTT ROI tracking

- Separate cost centre for the vertical in accounts.
- Every order tagged by stream (R1–R14), channel and campaign.
- Weekly time log by each team member working on the vertical.
- Marketing spend tagged by campaign; ROAS per campaign.
- Monthly P&L by stream and a one-page ROI summary for leadership.

Decision and phase-gate flow

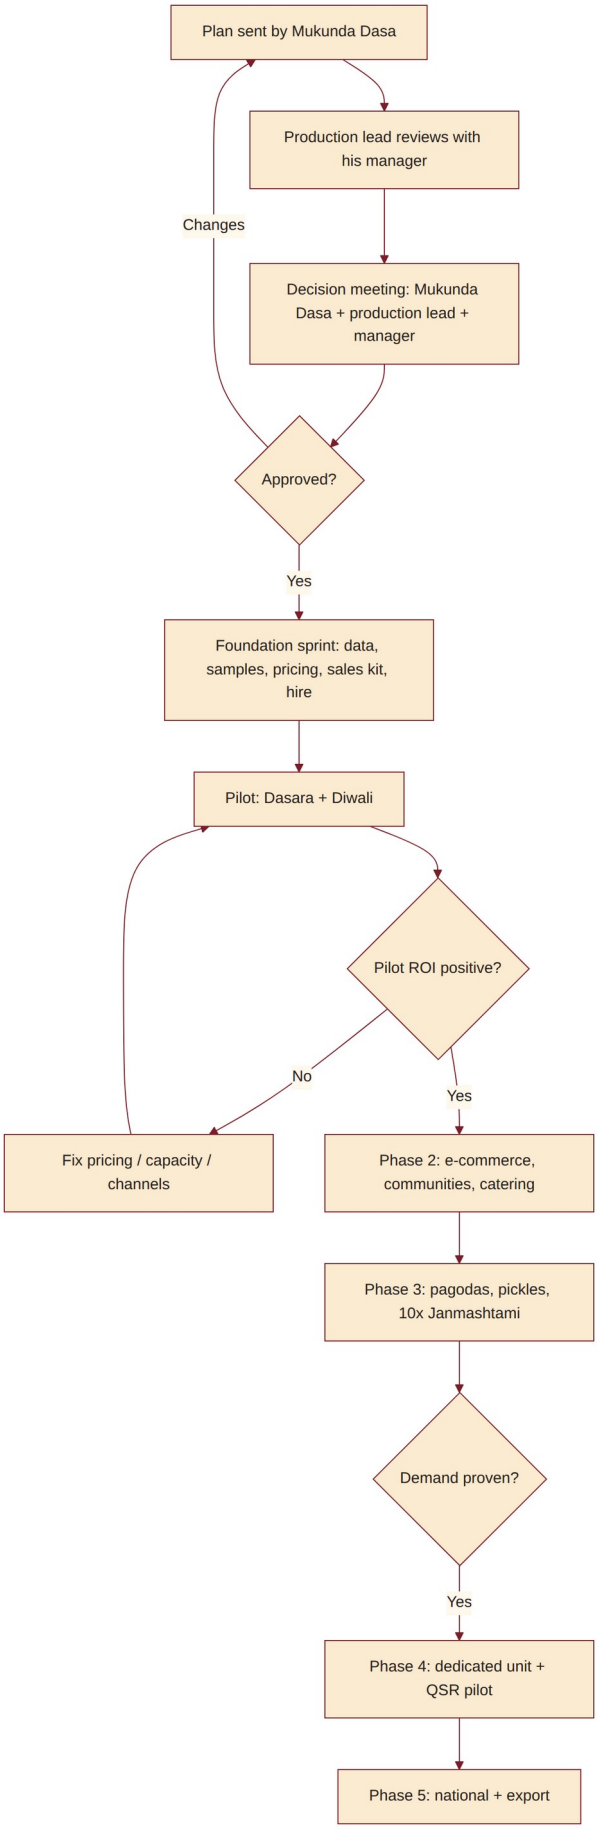

DMTT ROI tracking flow

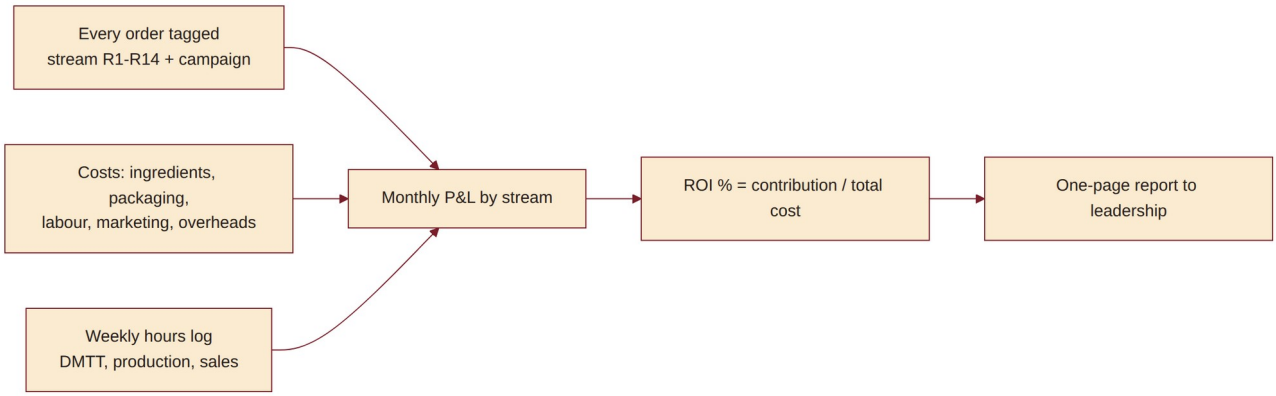

13. Change control

1. Any change to scope, budget above ₹1 lakh, pricing tiers or brand use is raised as a change request.
2. Project lead assesses impact on cost, time, capacity and risk within 3 working days.
3. Changes up to ₹5 lakh approved by project lead and production manager; above that by the sponsor.
4. Approved changes are logged in the tracker and communicated to all affected teams.

14. Issue and decision log

Date	Decision / issue	By	Status
26 Sep 2026	Two price segments (mass + premium) will run together	Meeting	Agreed
26 Sep 2026	All prasadam orders go only to the internal production lead	Mukunda Dasa	Agreed
26 Sep 2026	Shelf life of 15–20 days is the first product criterion	Meeting	Agreed
26 Sep 2026	Sugar acceptable where jaggery is too costly	Meeting	Agreed
26 Sep 2026	Weekly minimum order with fixed delivery day	Meeting	Agreed
26 Sep 2026	Start with internal demand before external expansion	Meeting	Agreed
—	Brand name to use on packs	Sponsor	Open
—	Budgets per department	Mukunda Dasa	Open

15. Action items

#	Action	Owner	Due
A1	Provide the order confirmation information requested for prasadam orders	Production team (order coordinator)	29 Sep 2026
A2	Hire an additional person for prasadam production work	Production lead	10 Oct 2026
A3	Propose available budget and requested items to production for samples and planning	Mukunda Dasa's team	30 Sep 2026
A4	Analyse 6–12 months of prasadam purchases and order volumes; share regular and festival estimates	DMTT data	3 Oct 2026
A5	Prepare and send the detailed plan for the prasadam and sweets vertical	Mukunda Dasa	30 Sep 2026 (this document)
A6	Identify additional prasadam products with longer	Production lead	4 Oct 2026

	shelf life		
A7	Prepare packaging and product presentation for bulk corporate gifting	DMTT designer + Production lead	10 Oct 2026
A8	Send a representative to support meetings with large company owners	Mukunda Dasa	3 Oct 2026
A9	Hold the finalisation meeting on products and quantities	Mukunda Dasa	5 Oct 2026
A10	Route all prasadam orders only to the internal production lead	All departments	Immediate
A11	Get pagoda costing done	Facilities	31 Oct 2026
A12	Respond to the Chinmaya Mission 50,000-meal request	Mukunda Dasa	Immediate

Open questions

- Final product list, quantities and weekly minimum per department?
- Budget allocated for prasadam per department (LLP, Culture Connect, online donors)?
- Pricing model split between premium and competitive tiers?
- Real production capacity per day now, with one more hire, and at peak with seasonal staff?
- Which infrastructure and staffing investments are justified before demand is validated?
- Brand name on packs: 'ISKCON Hyderabad', 'Hare Krishna Golden Temple', or a sub-brand?
- Which FSSAI licence covers commercial sale and e-commerce, and does it cover off-site stalls?
- Transfer-pricing and profit-sharing between production and marketing teams?
- Who owns catering for very large orders (50,000 meals) until a catering unit exists?
